



Downtown Flagler Street Beautification Project

Recap of work done in the month of May 2022

Milestones achieved in May 2022

Phase A (Biscayne Blvd to SE 3rd Ave) work completed by Lanzo:

- Roadway reconstruction
- Tree grate curb supports
- Installation of tree grates
- Installation of irrigation
- Brick paver installation
- Installation of concrete sidewalks
- Smart city pull box installation
- Installation of lighting conductor & fixers
- Installation of street furniture
- Installation of trench drain grates
- Landscape installation
- Placement of structural asphalt
- Cleaning of drainage structures
- Installation of signs
- Pressure cleaning of all surfaces
- Temporary stripping
- Harmonization
- Substantial completion awarded on May 13, 2022

Milestones achieved in May 2022

Phase B (SE 3rd Ave to E 2nd Ave) work completed by Lanzo:

- Installation of trees
- Installation of irrigation
- Tree grate curb supports
- Installation tree outlet conduit
- Installation of rail
- Installation of brick pavers
- Installation tree outlet conduit
- Installation light poles& fixers
- Installation of Smart City pull boxes
- Casted foundations for furniture
- Sidewalk construction
- Utility adjustments
- Installation of signpost

Phase B (SE 3rd Ave to E 2nd Ave) work completed by FP&L Subcontractor:

- Completed repairs on FPL vaults in Section B on May 19 & 20, 2022


Milestones achieved in May 2022

Phase C (E 2nd Ave to E 1st Ave) work completed by Lanzo:

- Closure of Section C started on May 16, 2022
- Installation of Construction fence
- Milling of existing asphalt
- Clearing and grubbing of sidewalk & curb



Installation of signs section A

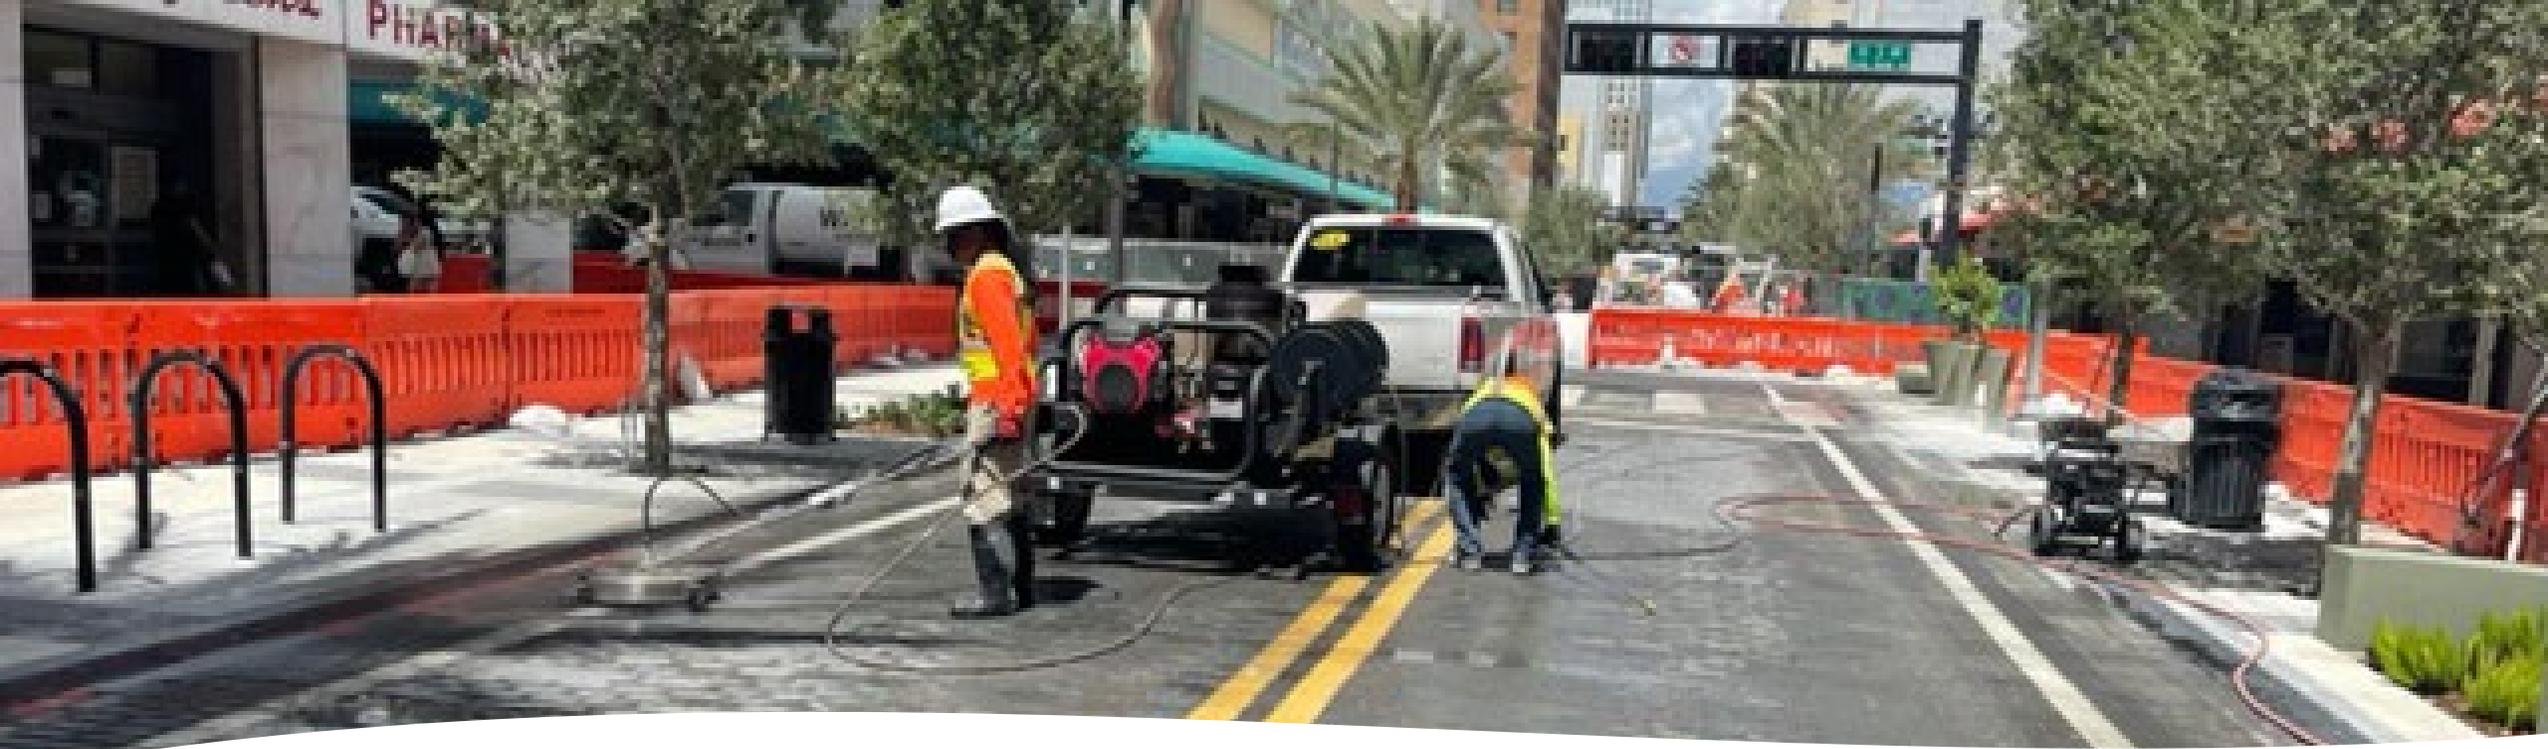

Pressure cleaning section A

Installation of
landscape section A



Installation of shrubs
in section A





Installation of
trench drain grates
section A

Installation of lighting
conductor in section A





Installation of furniture in section A



Removal of longitudinal channelizing devices in section A



Installations of light poles
section B



Casting of tree grate curb supports section B

Installation of Palm trees section B





Installation of fence in section C

Demolition/clearing &
grubbing section C





Milling of existing asphalt section C
